



EARTHQUAKE SAFETY & EMERGENCY RESPONSE BOND 2010

FIRE STATION NO. 16 REPLACEMENT

Issue #35
July 27, 2018

This project will provide a new seismically safe facility for the San Francisco Fire Department.

GENERAL INFO

Project Updates

- Sidewalk closed on Pixley Street until mid-August due to installation of new site utilities, placement of new concrete sidewalk, and planting new street trees.
- Ceramic wall and floor tiling and installation of plumbing fixtures in the 1st floor public restroom, 2nd floor men and women's restrooms, and officers' restrooms is complete.
- HVAC rough-in throughout building is complete.
- Installation of aluminum curtainwall and operable windows at north elevation is complete.
- Installation of turnout gear lockers in app bay is complete.
- **Weekend work is scheduled to occur on Saturday, 7/28.**

Activities Week of 7/30/2018 - 8/4/2018

- Application of stucco finish coat at rooftop penthouse and exterior elevations.
- Installation of stone veneer panels at south elevation.
- Installation of curtainwall glazing at north elevation.
- **Weekend work is scheduled to occur on Saturday, 8/4.**

Activities Week of 8/6/2018 - 8/11/2018


- Sitework and landscaping at Pixley Street sidewalk.
- Installation of acoustic ceiling tiles at 1st and 2nd floors.
- Painting at exterior elevations.
- Building department inspections and begin commissioning of mechanical systems.
- **Weekend work is scheduled to occur on Saturday, 8/11.**

Other Information

- SFFD will be responding from nearby Fire Stations 10 and 51; fire service will continue uninterrupted.
- sf-fire.org/temporary-fire-station-closure-service-status
- View construction progress photos and subscribe to this newsletter: sfearthquakesafety.org/firestation16

SCHEDULE

*Construction schedule is subject to change due to weather or unforeseen conditions.

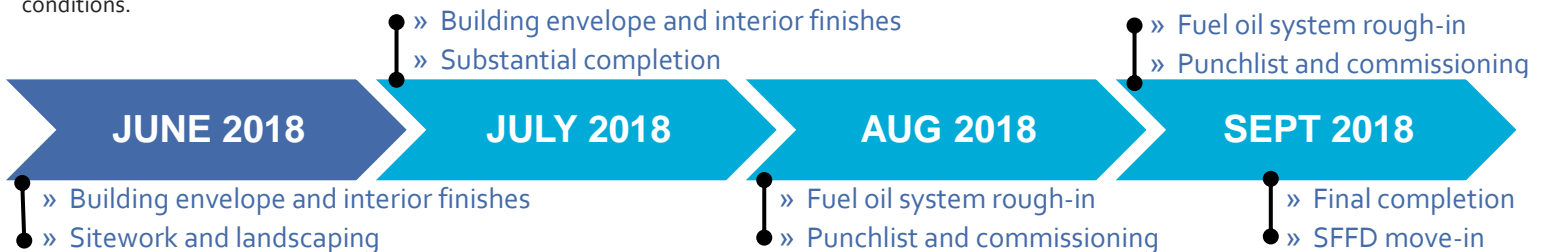

RedGard Waterproofing Membrane Applied to Stucco at South Elevation on Pixley Street (July 25, 2018)



Firefighters' Turnout Gear Lockers in the Apparatus Bay (July 25, 2018)

For more information:

M. Magdalena Ryor, Project Manager
Magdalena.Ryor@sfdpw.org
(415) 557-4659

For immediate service regarding construction issues:

Rob Rowland, Construction Inspector
Robert.Rowland@sfdpw.org
(415) 264-2511

For emergencies:

Roebuck Construction
Jeff Davino, Superintendent
(415) 716-0952
