



EARTHQUAKE SAFETY & EMERGENCY RESPONSE BOND 2010

FIRE STATION NO. 16 REPLACEMENT

Issue #27
February 9, 2018

This project will provide a new seismically safe facility for the San Francisco Fire Department.

GENERAL INFO

Project Updates

- Placed concrete deck at roof level on Thursday, 2/1.
- Weekend work is scheduled to occur on Saturday, 2/10.**

Activities Week of 2/12/2018 - 2/17/2018

- Install metal stud framing at 2nd floor interior.
- HVAC, electrical, and plumbing rough-in at 1st floor level.
- Concrete pour at roof level for equipment curbs is schedule for Thursday, 2/15. **Contractor will facilitate access for Pixley Street residents only. Watch for traffic control and flaggers.**
- Weekend work is tentatively scheduled to occur on Saturday, 2/17.**

Activities Week of 2/19/2018 - 2/24/2018


- Finish installation of metal stud framing at 2nd floor interior.
- Install metal stud framing at roof level exterior.
- HVAC, electrical, and plumbing rough-in at mezzanine level.
- Weekend work is tentatively scheduled to occur on Saturday, 2/24.**

Other Information

- SFFD will be responding from nearby Fire Stations 10 and 51; fire service will continue uninterrupted. sf-fire.org/temporary-fire-station-closure-service-status
- View construction progress photos and subscribe to this Construction Newsletter: sfearthquakesafety.org/firestation16



Concrete Deck at Roof Level (February 7, 2018)

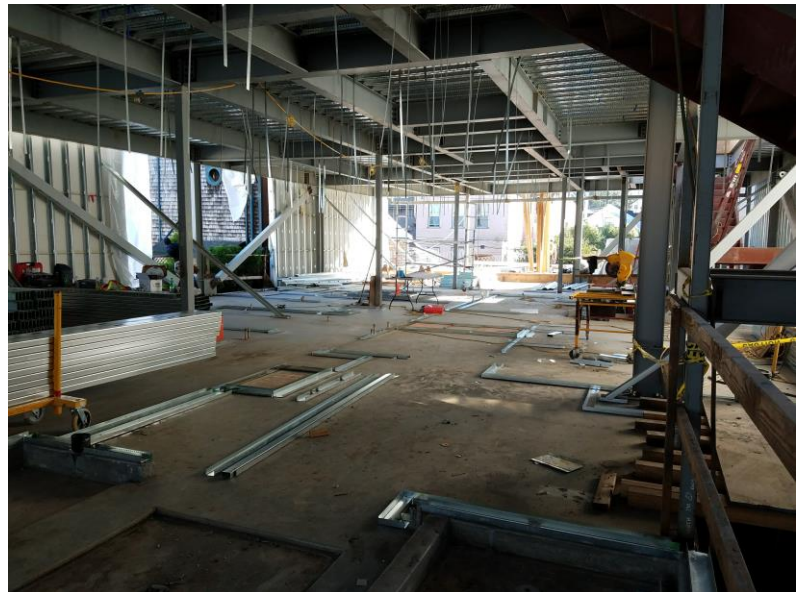

Interior Metal Stud Framing at 2nd Floor (February 7, 2018)

SCHEDULE

*Construction schedule is subject to change due to weather or unforeseen conditions.



For more information:

M. Magdalena Ryor, Project Manager
Magdalena.Ryor@sfdpw.org
(415) 557-4659

For immediate service regarding construction issues:

Rob Rowland, Construction Inspector
Robert.Rowland@sfdpw.org
(415) 264-2511

For emergencies :

Roebuck Construction
Jeff Davino, Superintendent
(415) 716-0952
