



# EARTHQUAKE SAFETY & EMERGENCY RESPONSE BOND 2010

## FIRE STATION NO. 16 REPLACEMENT

Issue #34  
June 8, 2018

This project will provide a new seismically safe facility for the San Francisco Fire Department.

### GENERAL INFO

#### Project Updates

- Sidewalk closed on Pixley Street until mid-July due to installation of infiltration trench, new site utilities, and placement of new concrete sidewalk.
- Installation of elevator is complete. It will provide access from the 1st floor to the roof, as required by ADA code.
- Installation of **four-fold apparatus bay doors** is complete. These new doors open and close quicker and are safer than traditional telescoping, sectional, and coiling doors.
- **Weekend work is scheduled to occur on Saturday, 6/9.**

#### Activities Week of 6/11/2018 - 6/16/2018

- Finish HVAC rough-in at the apparatus bay on 1st floor.
- Installation of aluminum curtain wall at north elevation facing Greenwich Street.
- Begin application of stucco at exterior elevations.
- Installation of ceramic floor tiles at 2nd floor men and women's locker rooms and restrooms.
- **Weekend work is scheduled to occur on Saturday, 6/16.**

#### Activities Weeks of 6/18/2018 - 6/23/2018


- Finish electrical rough-in at the apparatus bay on 1st floor.
- Begin installation of curtain wall glazing at north elevation facing Greenwich Street.
- Finish carpentry and casework at 1st and 2nd floors.
- **Weekend work is scheduled to occur on Saturday, 6/23.**

#### Other Information

- SFFD will be responding from nearby Fire Stations 10 and 51; fire service will continue uninterrupted.
- [sf-fire.org/temporary-fire-station-closure-service-status](http://sf-fire.org/temporary-fire-station-closure-service-status)
- View construction progress photos and subscribe to this newsletter: [sfearthquakesafety.org/firestation16](http://sfearthquakesafety.org/firestation16)

### SCHEDULE

\*Construction schedule is subject to change due to weather or unforeseen conditions.

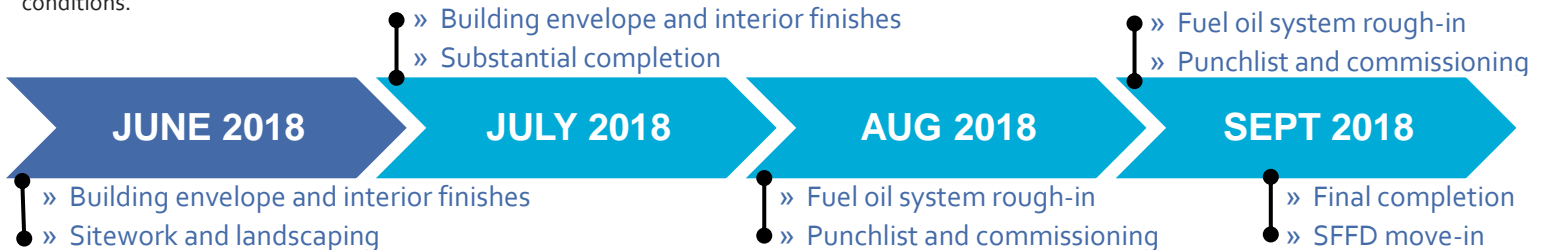

Installation of Curtainwall and Four-Fold Apparatus Bay Doors (June 6, 2018)



Installation of Ceramic Wall Tile at 2nd Floor Men's Restroom (June 6, 2018)

#### For more information:

M. Magdalena Ryor, Project Manager  
Magdalena.Ryor@sfdpw.org  
(415) 557-4659

#### For immediate service regarding construction issues:

Rob Rowland, Construction Inspector  
Robert.Rowland@sfdpw.org  
(415) 264-2511

#### For emergencies :

Roebuck Construction  
Jeff Davino, Superintendent  
(415) 716-0952
