



# EARTHQUAKE SAFETY & EMERGENCY RESPONSE BOND 2010

## FIRE STATION NO. 5 REPLACEMENT

Issue #27

September 24, 2018

This project will provide a new seismically safe facility for the San Francisco Fire Department.

### GENERAL INFORMATION

#### Project Updates

- The energy recovery ventilation (ERV) units at the main roof have been placed.
- Drywall at 2nd and 3rd floors' exterior and interior walls is substantially complete.
- Installation of brass firefighter slide poles is complete. Neoprene mats are installed at the base of the pole to help provide firefighters with a soft and safe landing.
- Drywall at 1st floor exterior walls is complete.
- Curtain wall aluminum framing at north, east, and south elevations is substantially complete.
- Installation of roof access hatch and ladder is complete.

#### Activities Week of 9/24/2018 - 9/29/2018

- Install windows at exterior elevations.
- Waterproof walls and floors at 3rd floor restrooms in preparation for ceramic wall and floor tiling.
- Install fuel system piping and electrical conduits at main roof.
- **Weekend work scheduled to occur on Saturday, 9/29.**

#### Activities Week of 10/1/2018 - 10/6/2018

- Prepare exterior elevations for installation of cement plaster and terracotta rainscreen systems.
- Install insulation and drywall at 1st floor interior walls.
- Continue installation of elevator.
- **Weekend work scheduled to occur on Saturday, 10/6.**

#### Other Information

- SFFD is responding from nearby Fire Stations 6 and 38; fire service will continue uninterrupted.
- [sf-fire.org/temporary-fire-station-closure-service-status](http://sf-fire.org/temporary-fire-station-closure-service-status)
- View construction progress photos and subscribe to this newsletter: [sfearthquakesafety.org/firestations](http://sfearthquakesafety.org/firestations)




ERVs Units Set at the Main Roof (September 11, 2018)



Brass Slide Poles and Landing Mats Installed (September 13, 2018)

### SCHEDULE

\*Construction schedule is subject to change due to weather or unforeseen conditions.

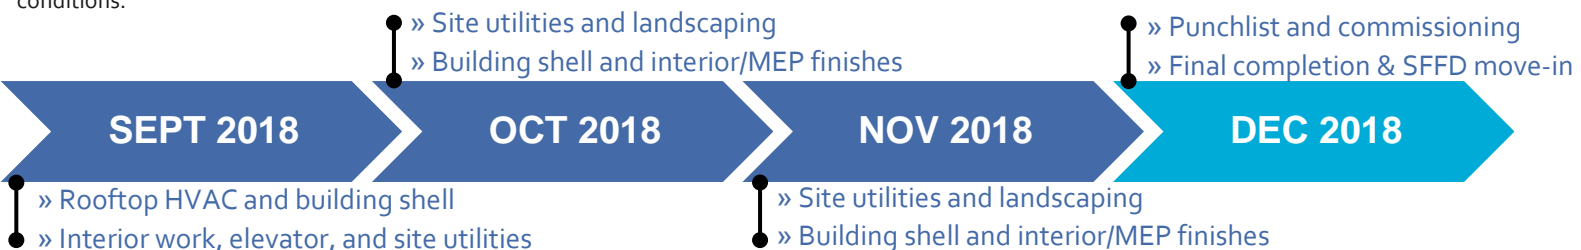

#### For more information:

M. Magdalena Ryor, Project Manager  
Magdalena.Ryor@sfdpw.org  
(415) 557-4659

#### For immediate service regarding construction issues:

Ray Birmingham, Construction Manager  
Ray.Birmingham@sfdpw.org  
(415) 244-9748

#### For emergencies:

Alten Construction  
Harry Torrano, Site Superintendent  
(415) 559-6063
