



# EARTHQUAKE SAFETY & EMERGENCY RESPONSE BOND 2010

## FIRE STATION NO. 5 REPLACEMENT

This project will provide a new seismically safe facility for the San Francisco Fire Department.

Issue #34  
April 15, 2019

### GENERAL INFORMATION

#### Project Updates

- Installed firefighters' lockers and storage cabinets.
- Installed platform beds at officers' quarters and firefighters' dormitory.
- Installed terracotta tile panels at exterior elevations.
- Installed four-fold apparatus bay doors at east elevation.
- Installed pedestal paver system at 3rd floor terrace.
- Placed permeable pavement and asphalt concrete at sideyard and parking lot area.
- Install fencing, gates, and gate hardware and painted parking lot striping at sideyard.
- Placed concrete bulb-out at corner of Turk Street and Webster Street. "Bulb-outs enhance pedestrian safety by increasing pedestrian visibility, shortening crossing distances, slowing turning vehicles, and visually narrowing the roadway" ([sfbetterstreets.org](http://sfbetterstreets.org)).

#### Activities Week of 4/15/2019 - 4/20/2019

- Install station identification signage at north and east elevations.
- Plant one Victorian Box tree at sidewalk on Turk Street and one Chinese Elm tree at sidewalk on Webster Street. Development projects are required to plant Street Trees in accordance with Section 806 of the Public Works Code.
- Install murphy bed at communications room at 1st floor.
- Punchlist work throughout site and building.
- **Weekend work to occur on Saturday, 4/20.**

#### Activities Week of 4/22/2019 - 4/27/2019

- Punchlist work throughout site and building.
- **Weekend work to occur on Saturday, 4/27.**

#### Activities Week of 4/29/2019 - 5/4/2019


- Final inspections by the Building Department (DBI).
- **Ribbon Cutting Ceremony scheduled for May 1st, 11am at Fire Station No. 5, 1301 Turk Street.**

#### Other Information

- SFFD is responding from nearby Fire Stations 6 and 38; fire service will continue uninterrupted.
- [sf-fire.org/temporary-fire-station-closure-service-status](http://sf-fire.org/temporary-fire-station-closure-service-status)
- View construction progress photos and subscribe to this newsletter: [sfearthquakesafety.org/firestation5](http://sfearthquakesafety.org/firestation5)



Four-Fold Apparatus Bay Doors at East Elevation (April 13, 2019)

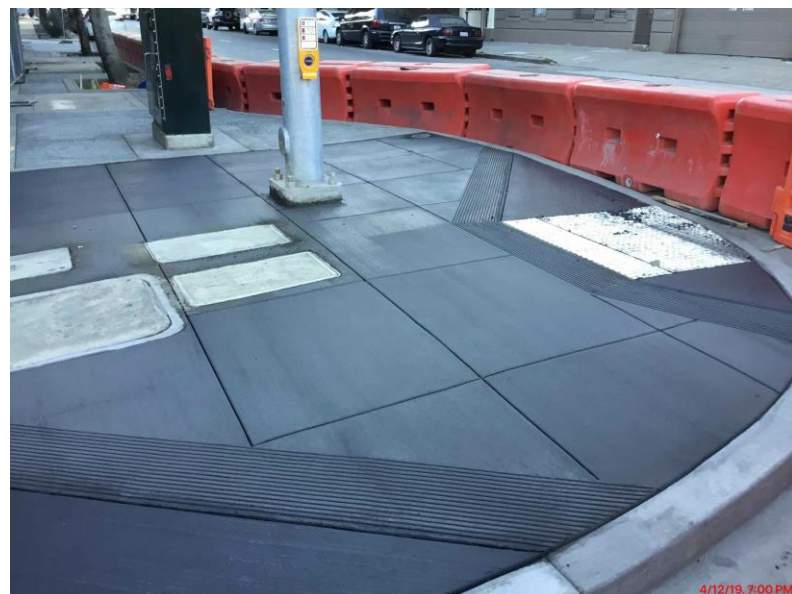

Concrete Bulb-Out at Corner of Turk St. and Webster St. (April 13, 2019)

### SCHEDULE

\*Subject to change due to weather or unforeseen conditions.

**APRIL 2018**

- » Punchlist work, commissioning, startup, and testing
- » Substantial completion and SFFD move-in
- » **Ribbon cutting ceremony on May 1st at 11am**

#### For more information:

M. Magdalena Ryor, Project Manager  
Magdalena.Ryor@sfdpw.org  
(415) 557-4659

#### For immediate service regarding construction issues:

Ray Birmingham, Construction Manager  
Ray.Birmingham@sfdpw.org  
(415) 244-9748

#### For emergencies:

Alten Construction  
Harry Torrano, Site Superintendent  
(415) 559-6063
