



EARTHQUAKE SAFETY & EMERGENCY RESPONSE BOND 2010

FIRE STATION NO. 5 REPLACEMENT

Issue #26

September 10, 2018

This project will provide a new seismically safe facility for the San Francisco Fire Department.

GENERAL INFORMATION

Project Updates

- Connection of fuel oil piping to emergency generator at main roof is complete. The generator will allow Fire Station 5 to remain operational for 72 hours after a major disaster. Please visit www.sf72.org for information on why its important to be prepared during the first 72 hours after a serious emergency.
- Installation of skylights and ductwork associated with rooftop exhaust fans is complete.

Activities Week of 9/10/2018 - 9/15/2018

- Trench work for connection of PG&E gas line to new facility.
- Installation of drywall at 1st floor exterior walls.
- Installation of suspended gypsum board ceiling at 2nd and 3rd floors.
- Installation of energy recovery ventilation (ERV) units and associated ductwork at main roof.
- Installation of curtainwall at north, east, and south exterior elevations.
- **Weekend work scheduled to occur on Saturday, 9/15.**

Activities Week of 9/17/2018 - 9/22/2018

- Waterproofing at interior walls of 3rd floor restrooms in preparation for ceramic tile installation.
- Installation of insulation and drywall at 1st floor interior walls.
- Installation of the elevator is in progress. Elevator work is anticipated to finish by the end of September.
- **Weekend work scheduled to occur on Saturday, 9/22.**

Other Information

- SFFD is responding from nearby Fire Stations 6 and 38; fire service will continue uninterrupted.
- sf-fire.org/temporary-fire-station-closure-service-status
- View construction progress photos and subscribe to this newsletter: sfearthquakesafety.org/firestations




Fuel Oil Piping to Generator at Main Roof (September 7, 2018)



Installation of Elevator (September 7, 2018)

SCHEDULE

*Construction schedule is subject to change due to weather or unforeseen conditions.

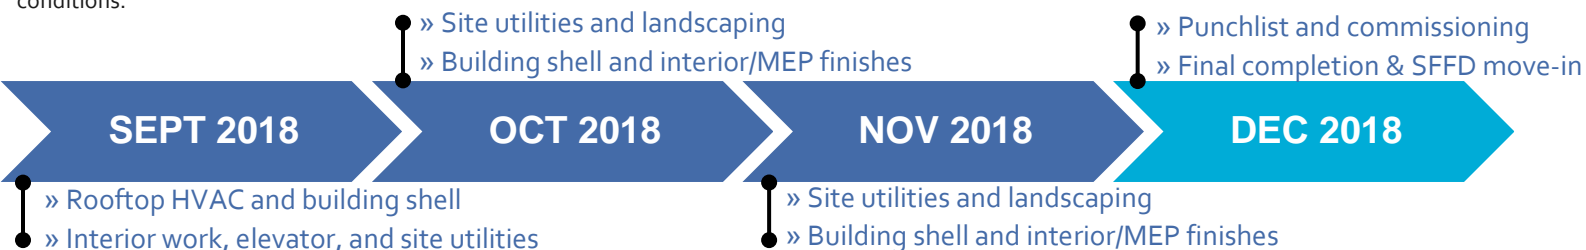

For more information:

M. Magdalena Ryor, Project Manager
 Magdalena.Ryor@sfdpw.org
 (415) 557-4659

For immediate service regarding construction issues:

Ray Birmingham, Construction Manager
 Ray.Birmingham@sfdpw.org
 (415) 244-9748

For emergencies:

Alten Construction
 Harry Torrano, Site Superintendent
 (415) 559-6063
